


# SISTRUNK SCHEDULE and ISSUE DOCUMENTATION


## Section 1 North

- Current Sched: Jul 2011– Nov '11
- Current Activities: Demo, light pole bases, sidewalk, curbing
- Upcoming Activities: Paver sidewalks, mill/overlay asphalt, and landscape.
- Issues: FPL neutral wire adjust, pole base placement due to conflict with existing utilities.

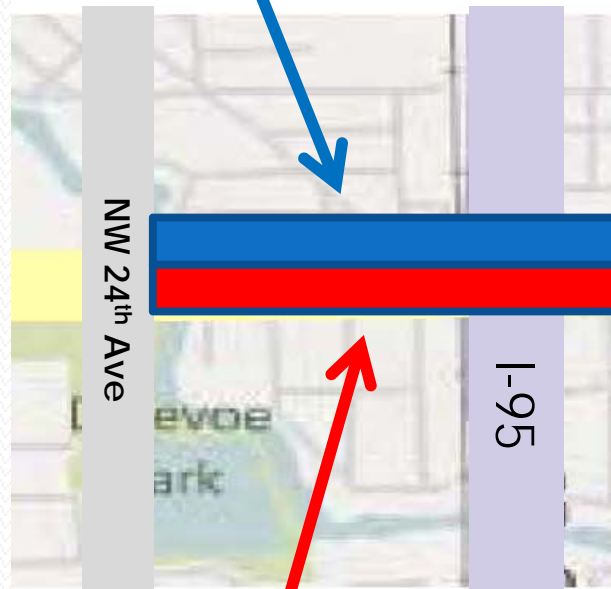


## Section 2 North

- Current Sched: Nov '11 – Apr '12
- Current Activities: Demo
- Upcoming Activities: Light poles and bases, signal mast arms, paver sidewalk, curbing, median irrigation, and landscape.
- Issues: Pole base placement due to conflict with utilities.

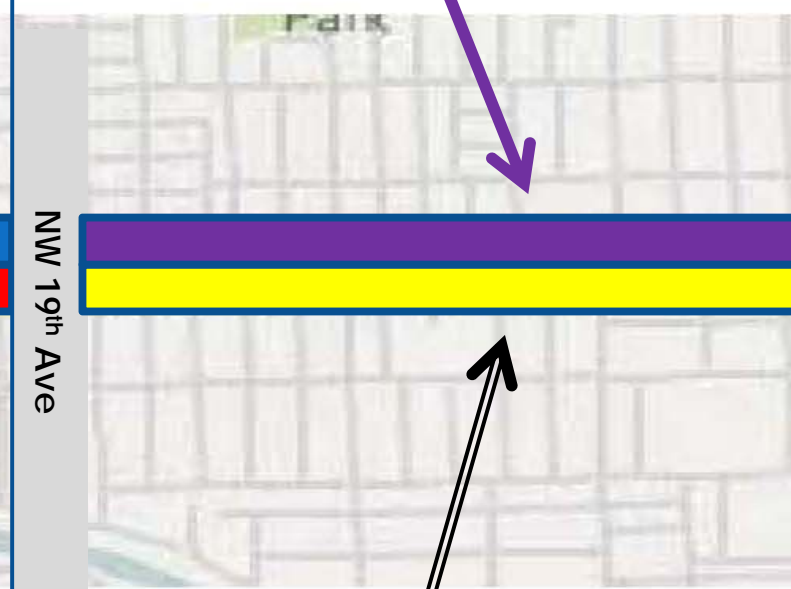


## Section 3 North

- Current Sch: Apr '12– Jul '12
- Current Activities: None
- Upcoming Activities: Demo, sidewalks, median irrigation, and landscape
- Issues: None

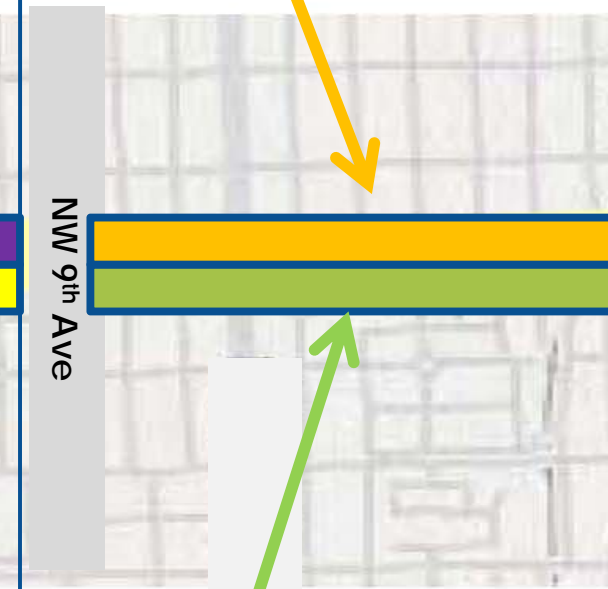

## Section 4

- Current Sch: Jan '11– Jan '12
- Current Activities: Demo, light poles, road base, and curbing
- Upcoming Activities Pavers, asphalt, irrigation and landscape.
- Issues: FPL pole removal, NE 3rd Ave light relocation, gas main relocation.

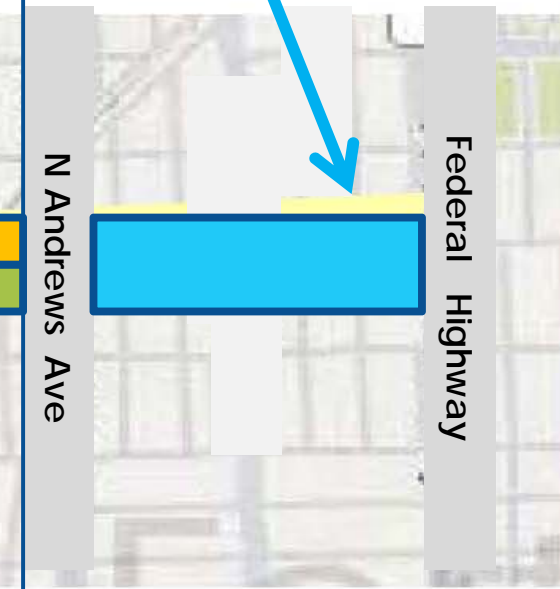

## Section 1 South

- Current Sched: Jan '11– Oct '11
- Current Activities: Light poles and bases.
- Upcoming Activities: Spread footers for light poles, mill and overlay asphalt, irrigation, and landscape.
- Issues: None

## Section 2 South

- Current Sched: Feb '11– Nov '11
- Current Activities: Pavers, light poles and bases, asphalt
- Upcoming Activities: Spread Footers for light poles, medians, irrigation and landscape.
- Issues: Pole base placement due to conflict with utilities.

## Section 3 South

- Current Sch: Apr '12 – Aug '12
- Current Activities: None
- Upcoming Activities: None
- Issues: FPL undergrounding, Jones limits of work coordination.



**SCHEDULE SUBJECT TO CHANGE and Subject to FPL Underground Schedule  
Does not include final lift of asphalt**

